

Name: Tarun Jagan
SRN: PES1UG24AM304

SE Lab – 2

1. Epics

The screenshot shows the Jira interface for the 'LAB2_SE LABS' space. The 'List' view is selected, displaying a table of 4 epics. The table has columns for checkboxes, a 'Work' column, 'Assignee', 'Reporter', and 'Priority'. The epics are listed as follows:

	Work	Assignee	Reporter	Priority
☐	> LSL-1 Epic 1: Project Submission & Showcase	Unassigned	TJ Tarun Jagan	Medium
☐	> LSL-2 Epic 2: Judging and Scoring	Unassigned	TJ Tarun Jagan	Medium
☐	> LSL-3 Epic 3: Public Voting and Leaderboard	Unassigned	TJ Tarun Jagan	Medium
☐	> LSL-4 Epic 4: Event Administration	Unassigned	TJ Tarun Jagan	Medium

At the bottom of the table, there is a '+ Create' button and a pagination indicator '4 of 4' with a refresh icon.

2. Stories

[illegible]

3. 1st Sprint

Search

+ Create

See plans

Spaces

LAB2_SE LABS

...

Summary

List

Board

Backlog

Development

Forms

Timeline

Reports

Docs

+

Complete sprint

To Do

0

In Progress

0

+ Create

In Review

4

Story 3.2: Prevent Duplicate Voting

Parent

Epic 3: Public Voting and Leaderb...

LSL-10

8

Story 3.3: View Real-Time Leaderboard

Parent

Epic 3: Public Voting and Leaderb...

LSL-11

5

Story 4.1: Create Expo Event

Parent

Epic 4: Event Administration

LSL-12

2

Story 4.2: Configure Judging and Voting Windows

Parent

Epic 4: Event Administration

LSL-13

3

+ Create

Done

0

+ Create

4. 2nd Sprint

Search

+ Create

See plans

Spaces

LAB2_SE LABS

...

Summary

List

Board

Backlog

Development

Forms

Timeline

Reports

Docs

+

Complete sprint

To Do0

+ Create

In Progress5

Story 1.1: Create Showcase Profile

Parent

Epic 1: Project Submission &... ▾

LSL-55

Story 1.2: Validate GitHub Repository URL

Parent

Epic 1: Project Submission &... ▾

LSL-63

Story 2.1: Submit Judge Score

Parent

Epic 2: Judging and Scoring ▾

LSL-75

Story 2.2: Define Rubric Criteria

Parent

Epic 2: Judging and Scoring ▾

LSL-83

Story 3.1: Cast Public Vote

Parent

Epic 3: Public Voting and Leaderb... ▾

LSL-95

+ Create


In Review0

+ Create


Done0

+ Create

5. Burndown Chart for 1st Sprint

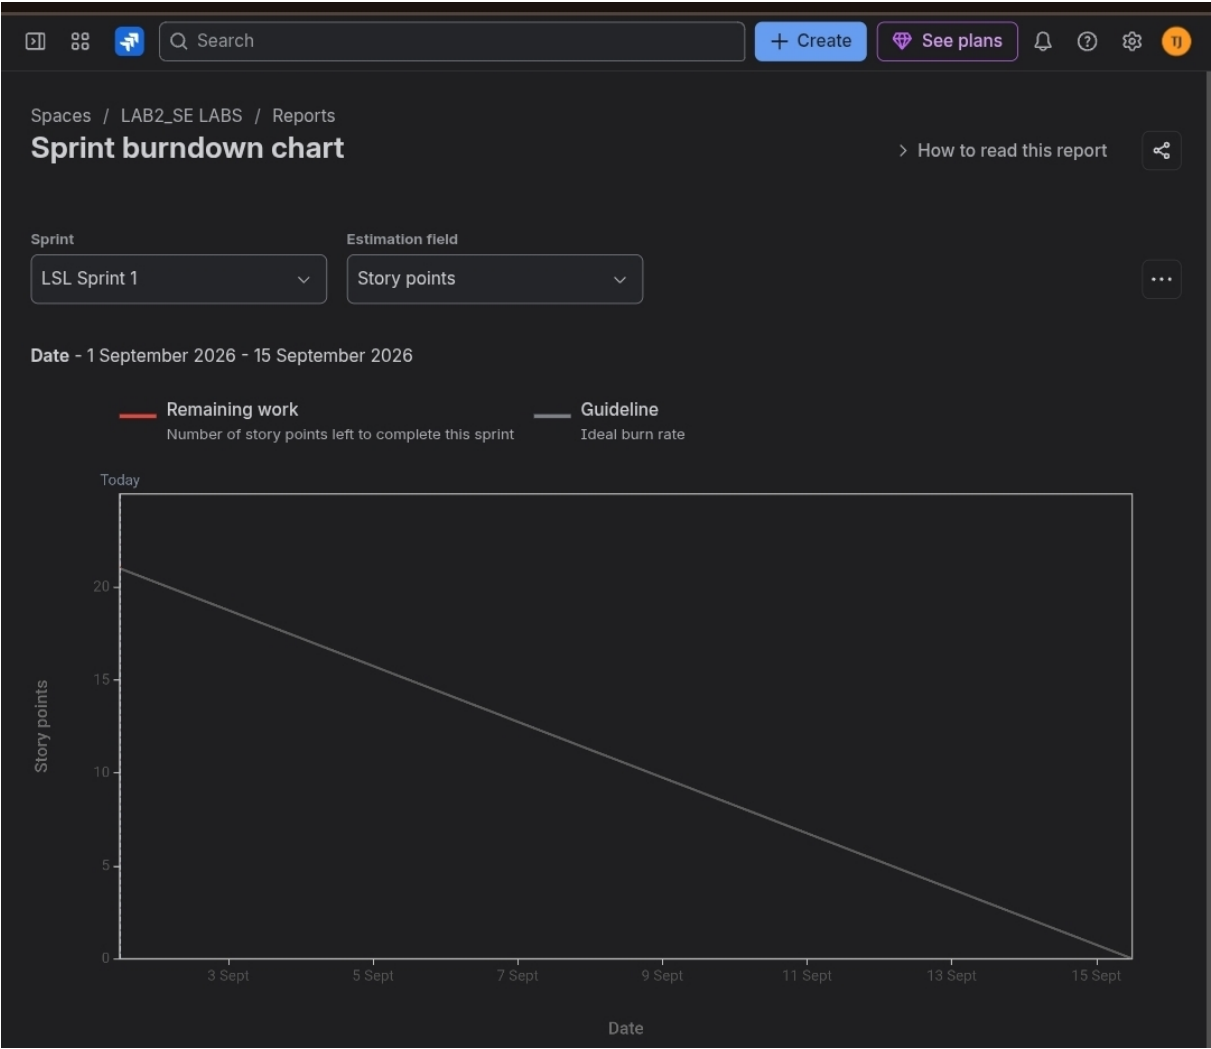

6. Burndown Chart for 2nd Sprint

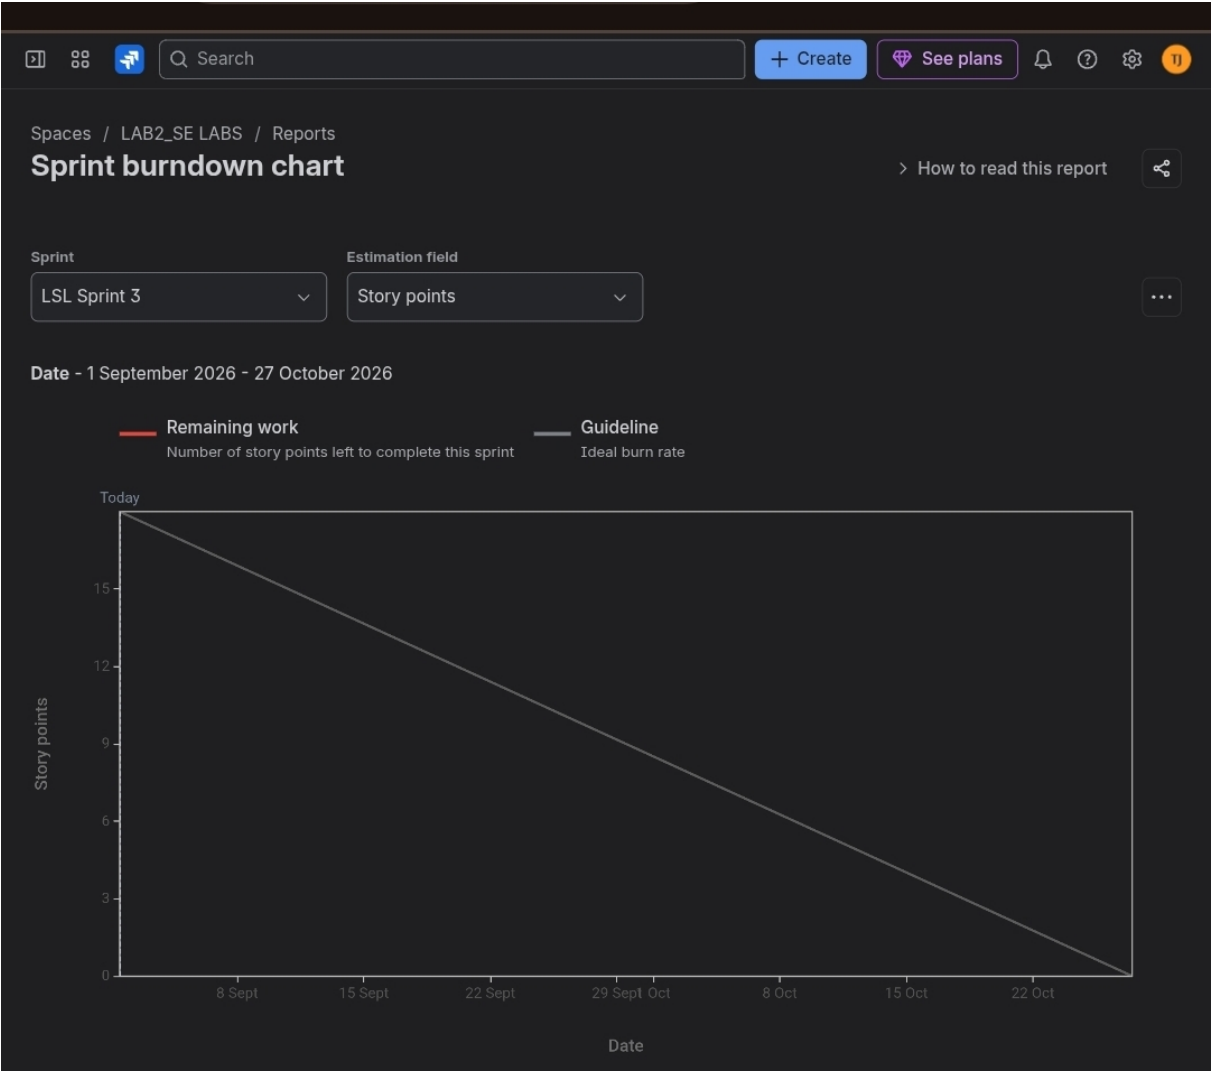

7. Reflection Questions

1. Did your estimations reflect the actual effort?

Mostly yes. The relative sizing held up well — Story 3.2 (Prevent Duplicate Voting) was correctly estimated as the most complex item at 8 points, since anti-sybil duplicate-vote logic genuinely carries more edge cases than a straightforward CRUD story like Story 4.1 (Create Expo Event, 2 points). Where the estimate fell short was duration: several stories were still "In Progress" or "In Review" rather than "Done" by the end of each sprint window, suggesting the points captured relative complexity accurately but the 1-week sprint box was tight for the full build-test-review cycle on the higher-point items.

2. Was your backlog well-prioritized?

Largely yes. The security- and core-flow-critical stories (duplicate-vote prevention, project submission, judge scoring) were correctly flagged High priority and pulled in early, while lower-impact configuration work (defining rubric criteria, configuring judging/voting windows) was left Medium priority and scheduled later. One improvement for next time: Epic 1 and Epic 2 stories (project submission, judging) logically feed the voting and leaderboard stories in Epic 3, so sequencing all of Epic 1/2 ahead of Epic 3 in Sprint 1 would have respected that dependency more cleanly than the split that was actually run.

3. How did your simulated sprint align with your plan?

Partially. Sprint 1 ended up carrying Stories 3.2, 3.3, 4.1, and 4.2 (18 points) and Sprint 2 carried Stories 1.1, 1.2, 2.1, 2.2, and 3.1 (21 points) — so the voting/admin work actually ran before the submission/judging work it logically depends on. In a real build this ordering would cause friction (testing voting before there are any judged, submitted projects to vote on). The simulation still achieved its goal of moving cards across To Do → In Progress → In Review, but a revised plan would sequence foundational stories (submission, judging) in Sprint 1 and build voting/leaderboard on top of them in Sprint 2.

4. What insights did the burndown chart give about your team's capacity?

Both burndown charts show the ideal guideline line declining smoothly toward zero, but neither shows a matching "remaining work" drop, since no stories were actually transitioned to Done within the simulated window — they stayed at In Review or In Progress. That's a useful capacity signal: committing 18–21 story points per 1-week sprint was more than could be fully closed out, which for a real team would be a cue to pull a smaller slice into each sprint (or to break larger stories like the 8-point duplicate-vote story into smaller sub-tasks) so that progress is visible as completed work rather than work-in-progress sitting at the review stage.
